


## MUGALIVAKKAM WSS

- Mugalivakkam is one among the 42 local bodies added in the expanded area of Chennai city. Mugalivakkam Town has an extent of 1.87 square Km. falls in Divisions 156, Area XII of Expanded Corporation of Chennai it consists of 375 streets. The total length of the road/streets for

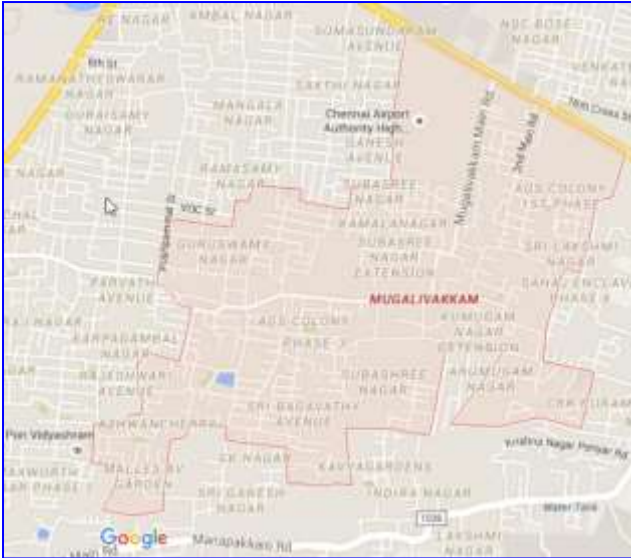

Mugalivakkam is 63.85 Km.

- The population to be benefited by implementation of Scheme is 28059, 49594 and 87655 for the year 2014, year 2029 and year 2044 respectively at the rate of water demand 4.36 MLD, 7.70 MLD and 13.61 MLD for the above corresponding years.
- The scheme cost for “Providing Comprehensive Water supply scheme to Mugalivakkam for a project value of Rs.3137.00 lakhs. The total project cost of Water supply and Sewerage scheme posed under CMCDM funds for the year 2013- 14 is Rs 51333.00 lakhs. The Government in its GO (MS) no 105 MAWS (MC.I) Department Dated 11.07.2013 has issued orders for the implementation of Chennai Mega City Development Mission.
- **The Components of work**
  1. Laying of DI Distribution mains of sizes ranging from 100mm to 450mm dia for a length of 59940 m.
  2. Laying of conveying mains of 200 mm - 400 mm DI pipes for a length of 2350 m.
  3. Construction of UGT 4.00 LL and OHT 10.00 LL and pump house at Arasamaram Mariamman Kulam and UGT 4.00 LL and OHT 10.00 LL and pump house at Madha Nagar.
  4. Providing House Service Connections for 24950 nos.

- **Contract details**

The work was awarded to M/s Shriram EPC Ltd. on 07.09.2016 for a contract value of Rs. 3008.04 lakhs. The works commenced on 19.09.2016. The contract period is 24 months.

➤ **Progress of work (as on 31.01.2017) :**

1. The physical progress so far achieved is 0.26%.  
0.57% of civil works in Over head tank, 0.57% of civil works in Underground tank and 0.57% pump house have been completed.
  
2. The financial progress so far achieved is 8.75%.
  
3. Schedule date of completion: September 2018.
