


## NANDAMBAKKAM WSS

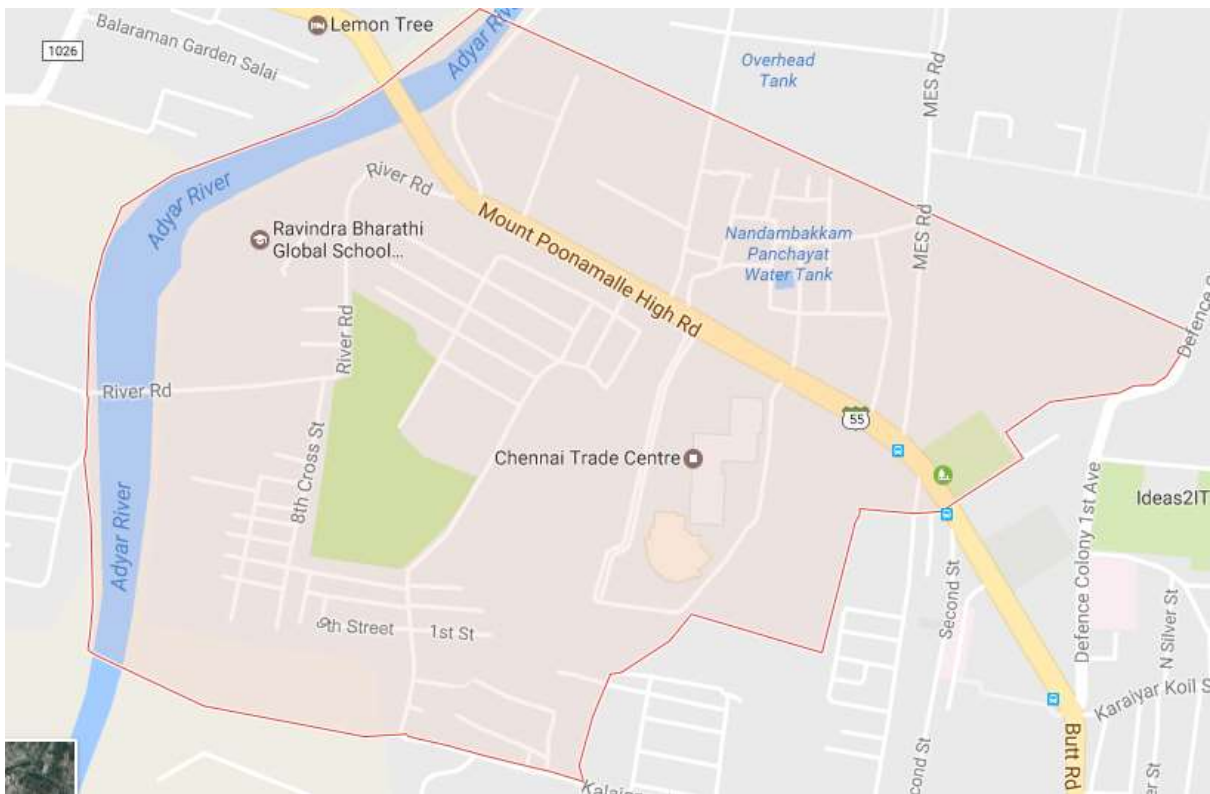

- Nandambakkam is one among the 42 Local bodies in the expanded area of Chennai City which falls in Greater Chennai Corporation division 158, Area XII (Alandur). The extent of area is 2.61 sq.km with 49 streets for a total length of 9.3 km.
- The population to be benefited by implementing the scheme are 7467, 13194 and 23321 in the years 2014, 2029 and 2044 respectively at the rate of 1.16 MLD, 2.05 MLD and 3.62 MLD in the corresponding years.
- The scheme cost for providing comprehensive water supply scheme to Nandambakkam is Rs.600 Lakhs. The funding pattern for this work is CMCDM 2012-13 and loan from TUFIDCO at Rs. 558 Lakhs and Rs. 42 Lakhs respectively.
- The Govt. in its G.O.(Ms).No.94, MA & WS (MC.1) Dept., Dt. 14.10.2012 has accorded administrative approved for this project. Technical sanction was made on 18.10.2012.

➤ **The Components of work:**

1. Laying of DI distribution mains of sizes ranging from 100mm to 400mm diameter for a length of 8400m.
2. Laying of conveying main of 200mm diameter DI pipes for a length of 190m.
3. Construction of UGT 2.0 LL at Ramar Koil Street – 1No.
4. Construction of OHT at 5.0 LL at Ramar Koil Street – 1No.
5. Providing House Service Connections for 980 Nos.

➤ **Contract details:**

The work has been awarded to M/s GKC-Vishwa consortium at a contract value of Rs.424 Lakhs on 21.10.2013 with a contract period of 18 months. The work was commenced on 21.02.2014. Schedule date of completion was 20.08.2015.

➤ **Progress of work (as on 31.05.2017)**

1. Physical progress - 97.5%
2. Financial Progress – 67.0%
3. Probable date of completion 30.09.2017.

